


Construction Area for Water Distribution Pipe Replacement Work in the Doyomaru (Koreishi) District and Surrounding Areas



General Layout of Water Distribution Pipe Installation Work

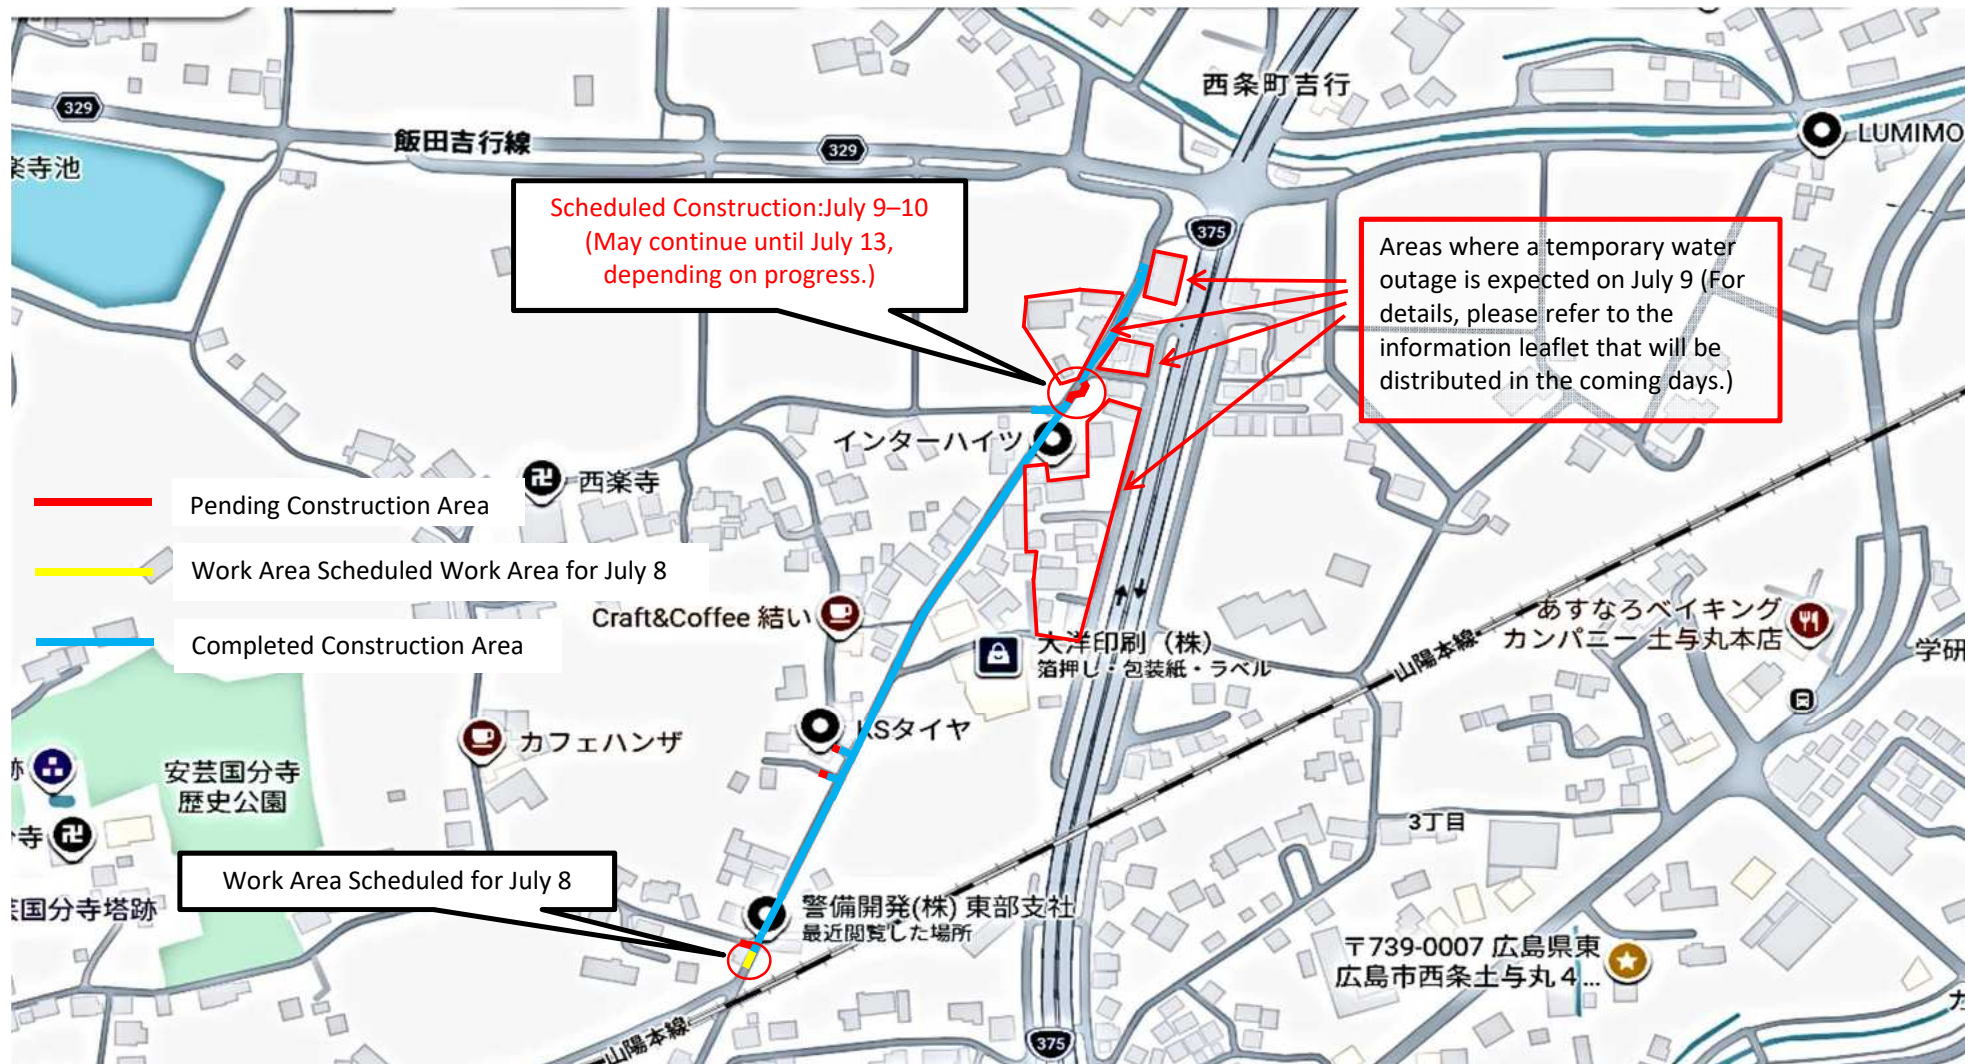

Water Main Installation (Approx. 449 m)

Completed (July. 7): 417.18 m

Progress: 93.0%

Traffic Restriction Area (July 7)

